

Oroville Facilities Relicensing FERC Project No. 2100 Process Update

Plenary Group Presentation

Oroville, California

December 16, 2003




Oroville Facilities Relicensing (Project No 2100)


Overall Schedule: 2000 to 2007



Oroville Facilities Relicensing (Project No 2100)

Overall Schedule: 2000 to 2007

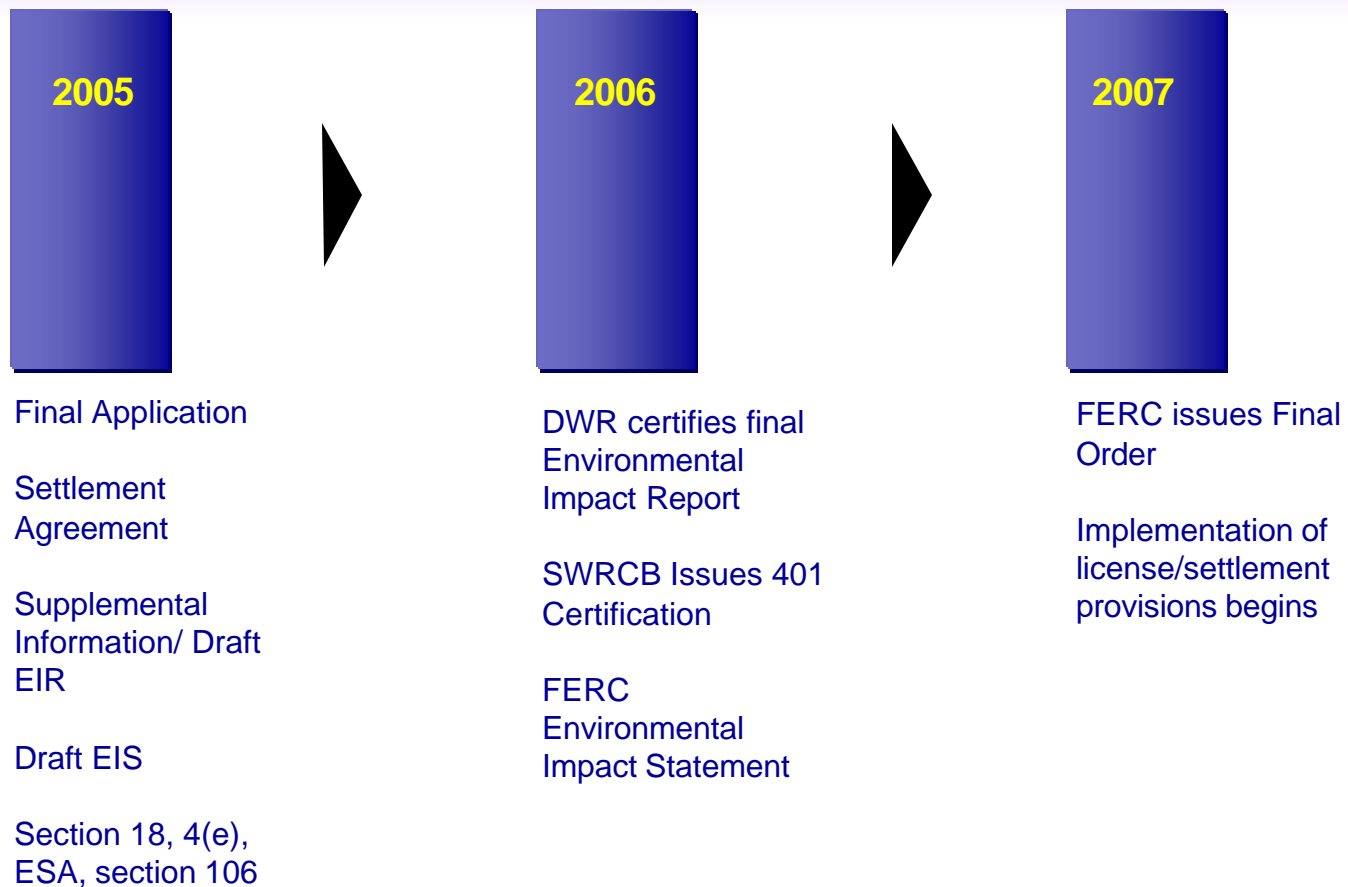

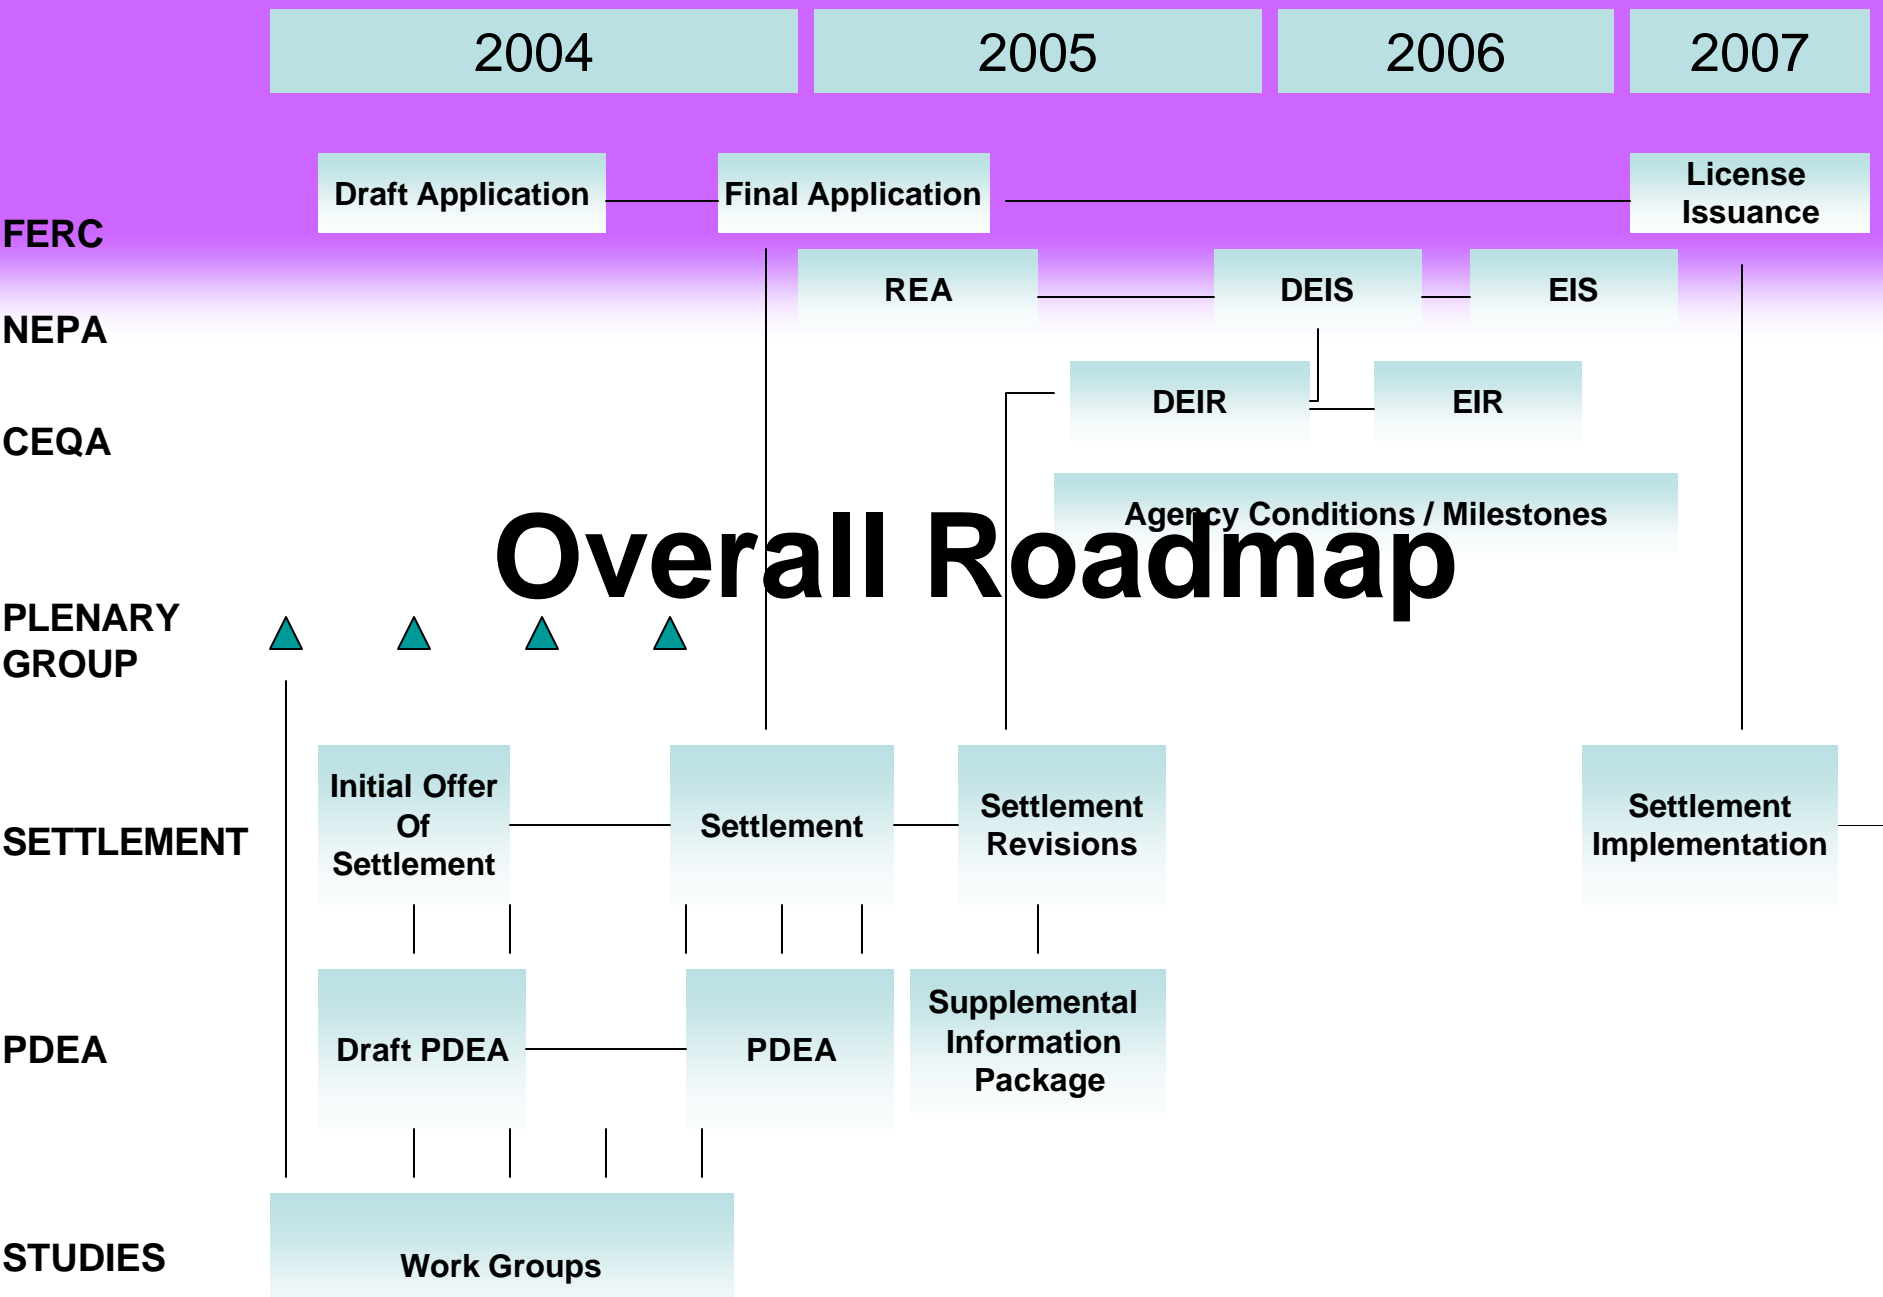

OROVILLE FACILITIES RELICENSING

COLLABORATIVE PROCESS SCHEDULE

THROUGH APPLICATION DEADLINE - January 31, 2005

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
Plenary Group													
Forward RAs for analysis	X	X											
Receive PDEA update				X									
Discuss PDEA/SA progress									X				X
Work Groups													
Submit RAs to Plenary Group													
Review study reports													
Develop narrative reports (Env)													
Stakeholder Activities													
Participate in ALP groups													
Obtain internal approvals											X	X	
Settlement Group(s)													
Request tech info/refine RAs													
Negotiate agreement		X	X	X	X	X	X	X	X	X			
Applicant Activities													
Provide SA, PDEA updates				X					X				X
Complete studies													
Prepare env. documents, SA													
<i>File application, PDEA, SA</i>													

