

Oroville Facilities Relicensing FERC Project No. 2100 Process Update




Plenary Group Presentation

Oroville, California

November 19, 2002



Oroville Facilities Relicensing Project No 2100 Overall Schedule: 2001 to 2007

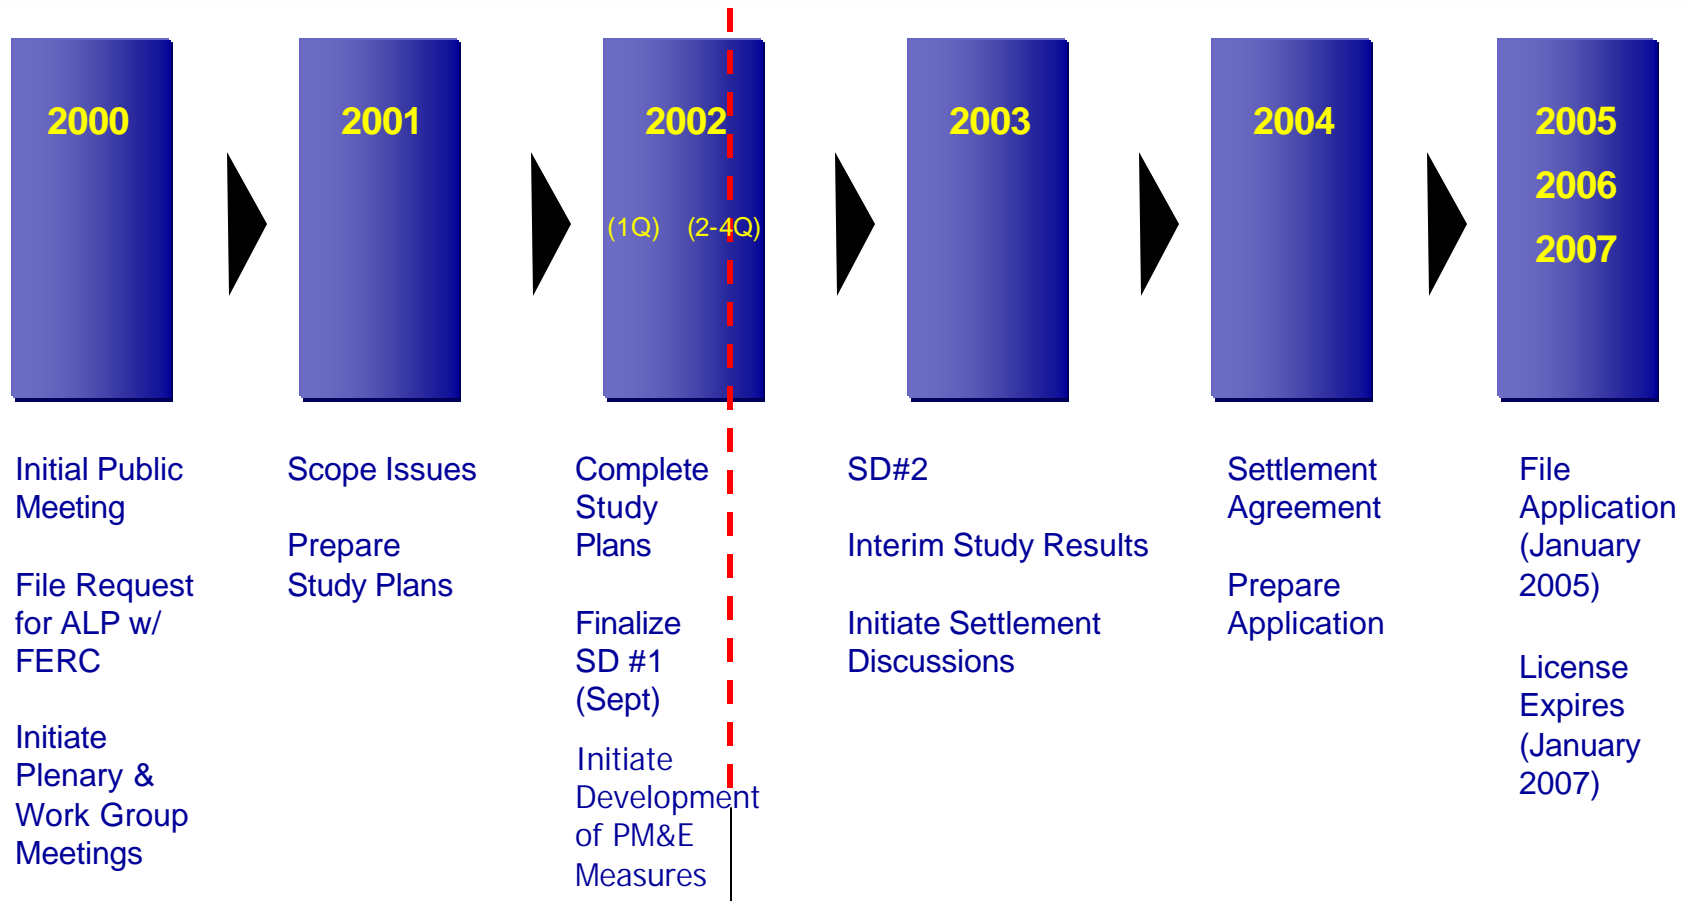

Scope
Issues

We are here –Implementing Studies/Initiating Development of PM&Es

2002

2003

2004

2005

2007

Study Implementation/Settlement Process

Study Implementation

*Determine Existing
Conditions/Project
Impacts**Develop, Screen, and
Evaluate PM&Es**Settlement Discussion/
Agreement***Environmental Document/Application**Study
Results

Oct '02

Initial
Results

June '03

Further
Results

Jan '04

Further Results
for Final License

March '04

Aug '04

Jan '02

Jan '03

Jan '04

Jan '05

SD-1
Sept '02SD-2
Feb '03Draft
Application/
APEA/DEIR
May '04Final
Application
APEA/DEIR
Jan '05FERC
Issues
License**Regulatory Integration***Draft Conditions**Final Conditions*

Plenary Group Milestones

2002

2003

2004

2005

2007

Study Implementation/Settlement Process

Plenary approves Task Force's Settlement Process Protocol, PM&E Development Framework, Screening Criteria (By Feb '03)

Plenary Group reviews preliminary identification and screening of PM&Es (By Jun '03)

Plenary Group reviews plans for environmental analysis of PM&Es/ Basis for Initiating Settlement Discussions (Mar '04)

Plenary Group approves Settlement Agreement/ Signing Ceremony (Nov '04)

Plenary Group approves resolution of outstanding issues post-filing (Date TBD)

Environmental Document/Application

Plenary Group input on SD2 components (Oct/Nov '02)

Plenary Group members provide comments on Draft Application/CEQA-NEPA Document (Issued May '04; Comment period ends Aug '04)

▲
SD-1
Sep '02

▲
SD-2
Feb '03

▲
Draft
Application/
APEA/DEIR
May '04

▲
Final
Application
APEA/DEIR
Jan '05

■
FERC
Issues
License

Regulatory Integration

Plenary Group reviews plans for regulatory integration/ coordinated environmental review (Oct '03)

Plenary Group reviews Draft/Final Conditions released by agencies (Date TBD)

Near-Term Plenary Group Schedule

November '02

- SD2 Document Component Discussion
- Fisheries Presentation
- Settlement Process Task Force Update

December '02

- Detailed Relicensing Roadmap
- Settlement Process Task Force Update

January '03

- Settlement Process Task Force Update/Approve Deliverables
- Present Draft SD2
- FERC requirements for Project Economics
