OROVILLE FACILITIES RELICENSING

DRAFT 2001 PROJECT SCHEDULE

ID	Task Name
1	**Alternative Licensing Procedure (ALP) Request**
2	**Receipt of FERC Approval for ALP Process**
3	**Six Month Progress Report**
4	**Develop and Approve Process Protocol**
5	Task Force
6	Plenary Review
7	Plenary Approval
8	**Initial Information Package (IIP)**
9	Management Review of IIP
10	Finalize IIP
11	Print IIP
12	Distribute IIP
13	**Public Reference File (PRF)**
14	Complete PRF
15	Maintain PRF
16	**NEPA Scoping**
17	Prepare Draft Scoping Document
18	Plenary Group Review
19	Task Force to Finalize SD
20	Plenary Group Approval
21	Finalize, Print & Distribute SD
22	FERC Issues Public Notice of Scoping
23	Site Visit / Scoping Meeting
27	Scoping Comments
28	**Initiate Application Process for 401 Cert.**
31	**File Notice of Intent w/FERC**
32	**Plenary Group**
33	Plenary Group Meeting (Group Structure/Roles)
34	Plenary Group Meeting (Follow up on Group Structure/Process)
35	Plenary Group Meeting (Follow up on Process/SD1)
36	Plenary Group Meeting (Scoping Document)
37	Plenary Group Meeting (Review Scoping Document Comments)

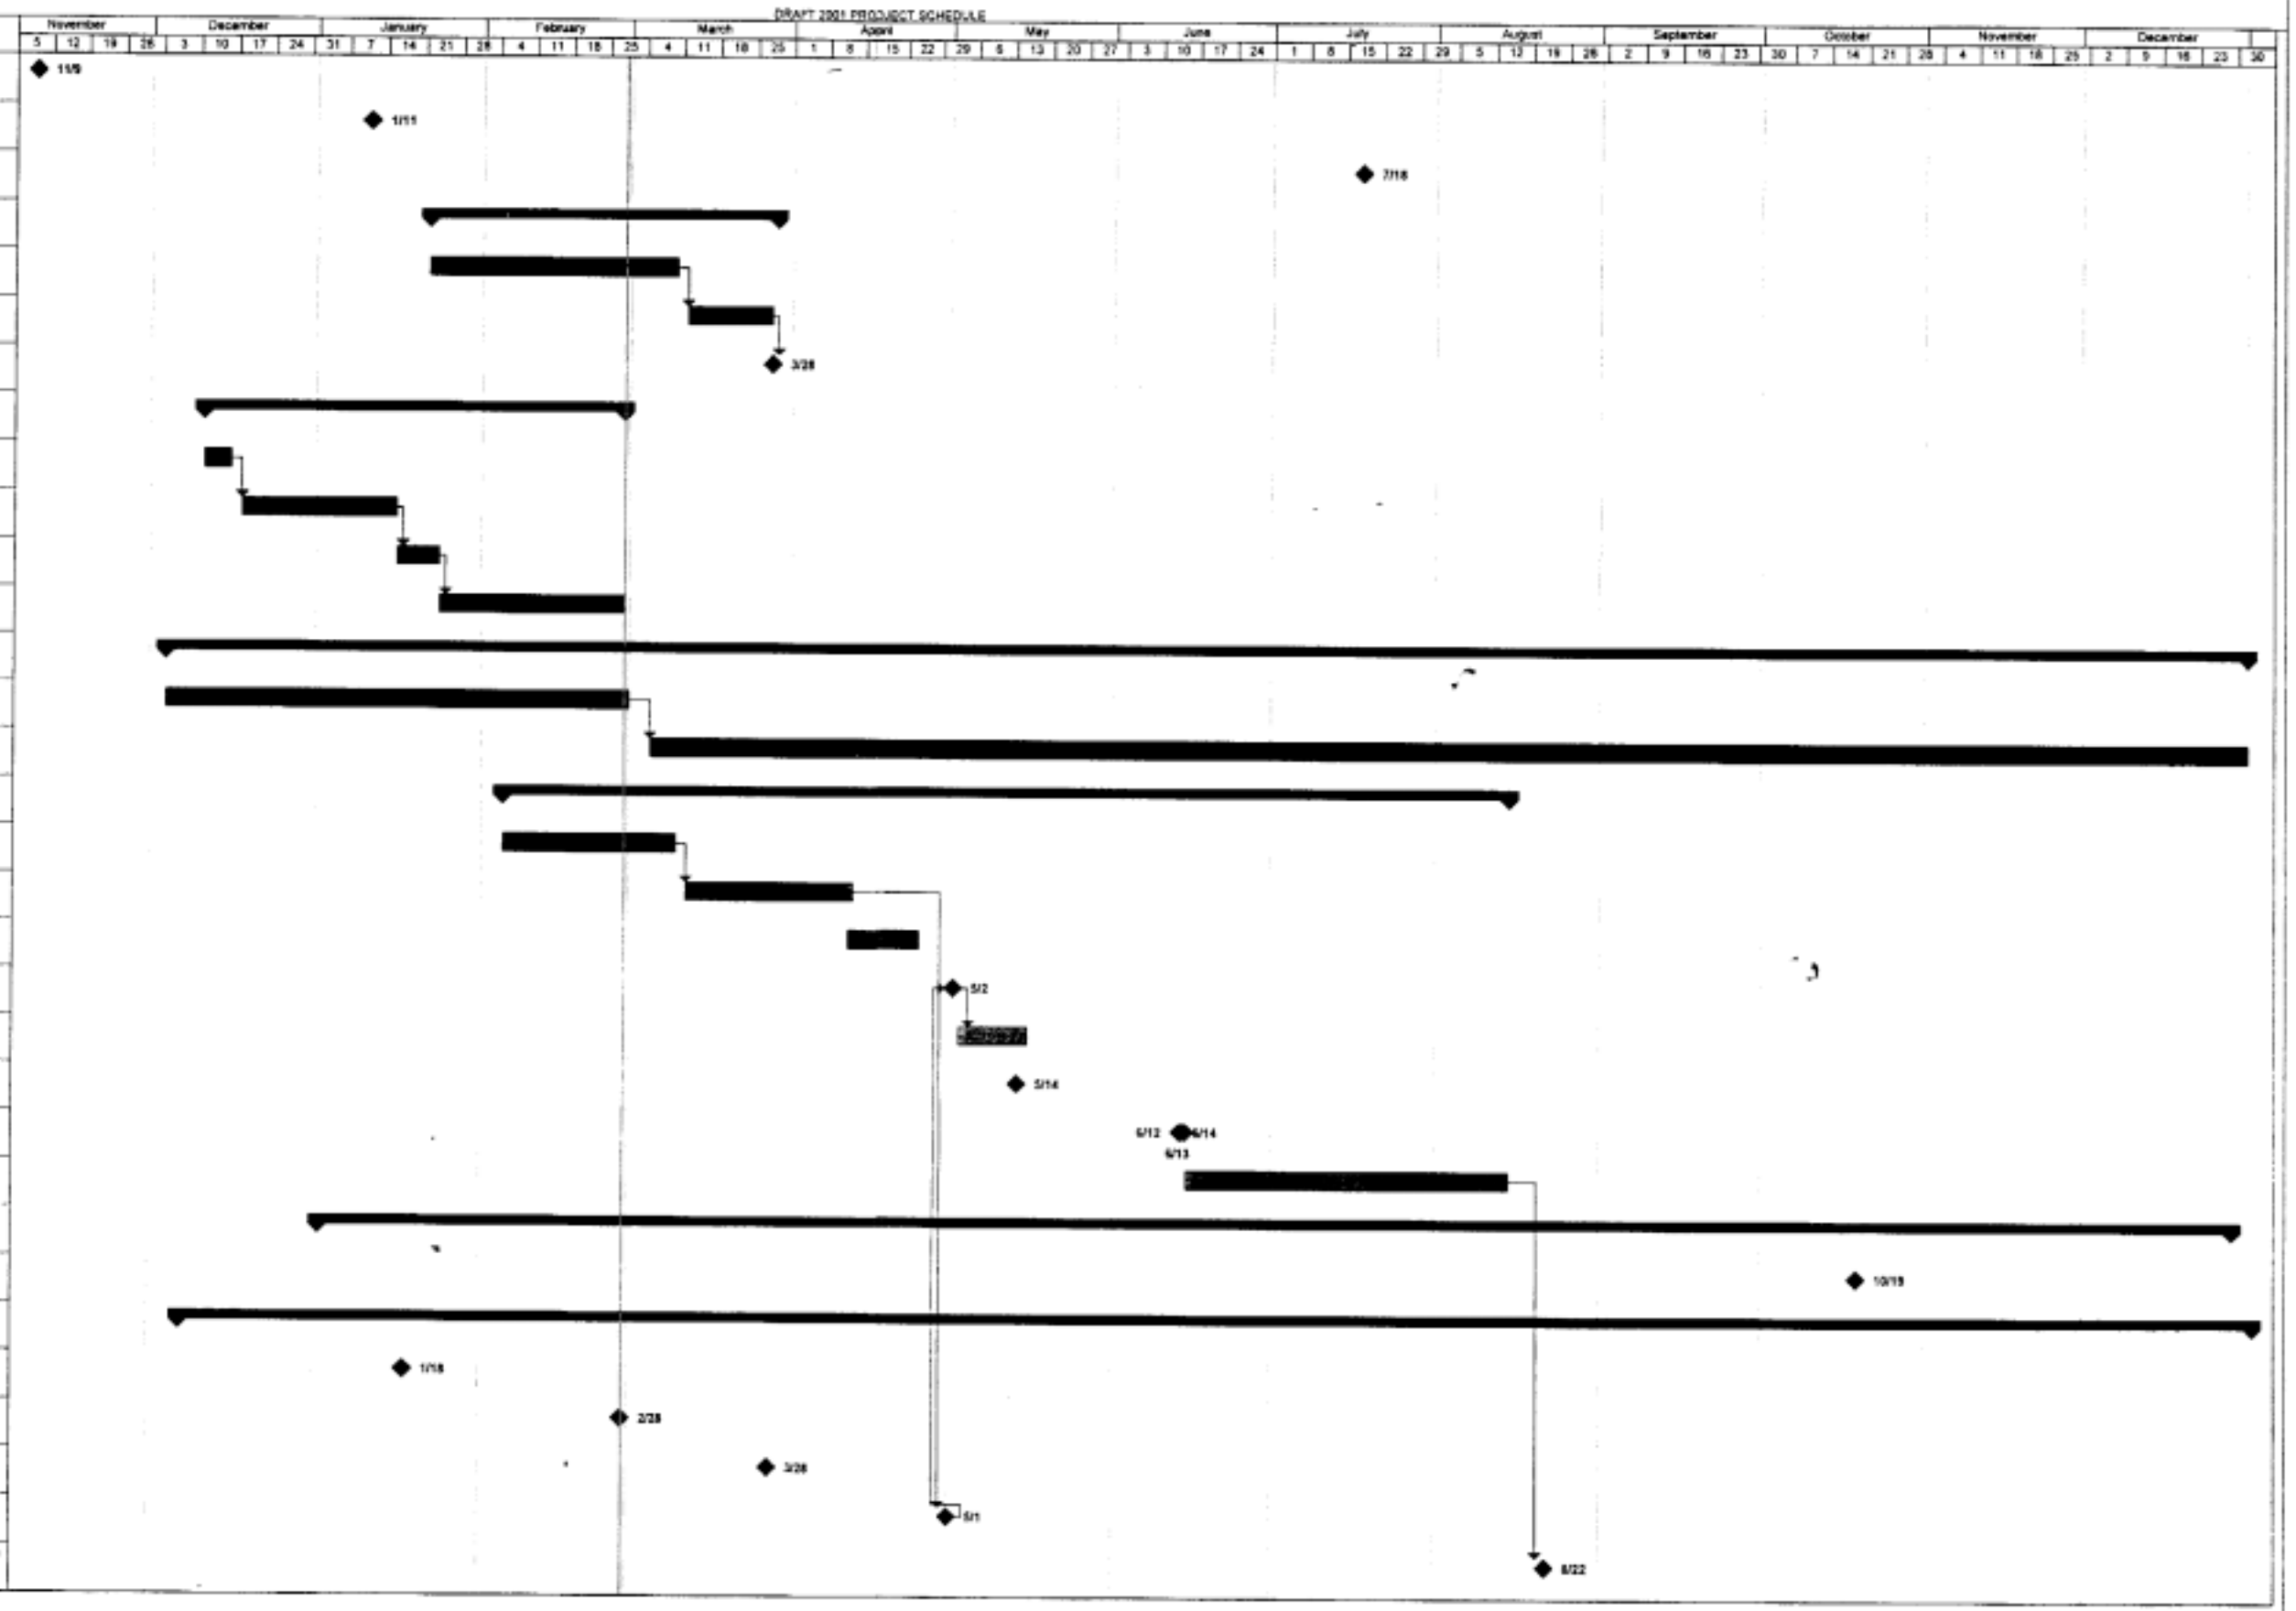

Project: OROVILLE FACILITIES REL
Date: Wed 2/28/01

Task | Task Progress | Critical Task | Critical Task Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary

OROVILLE FACILITIES RELICENSING

DRAFT 2001 PROJECT SCHEDULE

ID	Task Name
38	Plenary Group Meeting (Study Plan Approval)
39	**Work Groups**
40	**Issue Identification Meetings**
41	Recreation & Socioeconomics
45	Aquatics/Terrestrial
55	Operations & Engineering
58	Land Use & Visual Resources
61	Cultural Resources
64	**Issue Development Meetings**
65	Recreation & Socioeconomics
69	Aquatics/Terrestrial
72	Operations & Engineering
75	Land Use & Visual Resources
78	Cultural Resources
81	**Study Plan Development Meetings**
82	Recreation & Socioeconomics
88	Aquatics/Terrestrial
96	Operations & Engineering
102	Land Use & Visual Resources
106	Cultural Resources
110	**Mtg. To Discuss SD Comments Effects on Issues/Studie**
111	Recreation & Socioeconomics
112	Aquatics / Terrestrial
114	Operations & Engineering
115	Land Use & Visual Resources
116	Cultural Resources
117	**Compile & Transmit Study Plans**
118	**Prepare Study Plans**
119	Recreation & Socioeconomics
120	Aquatics
121	Terrestrial
122	Operations & Engineering

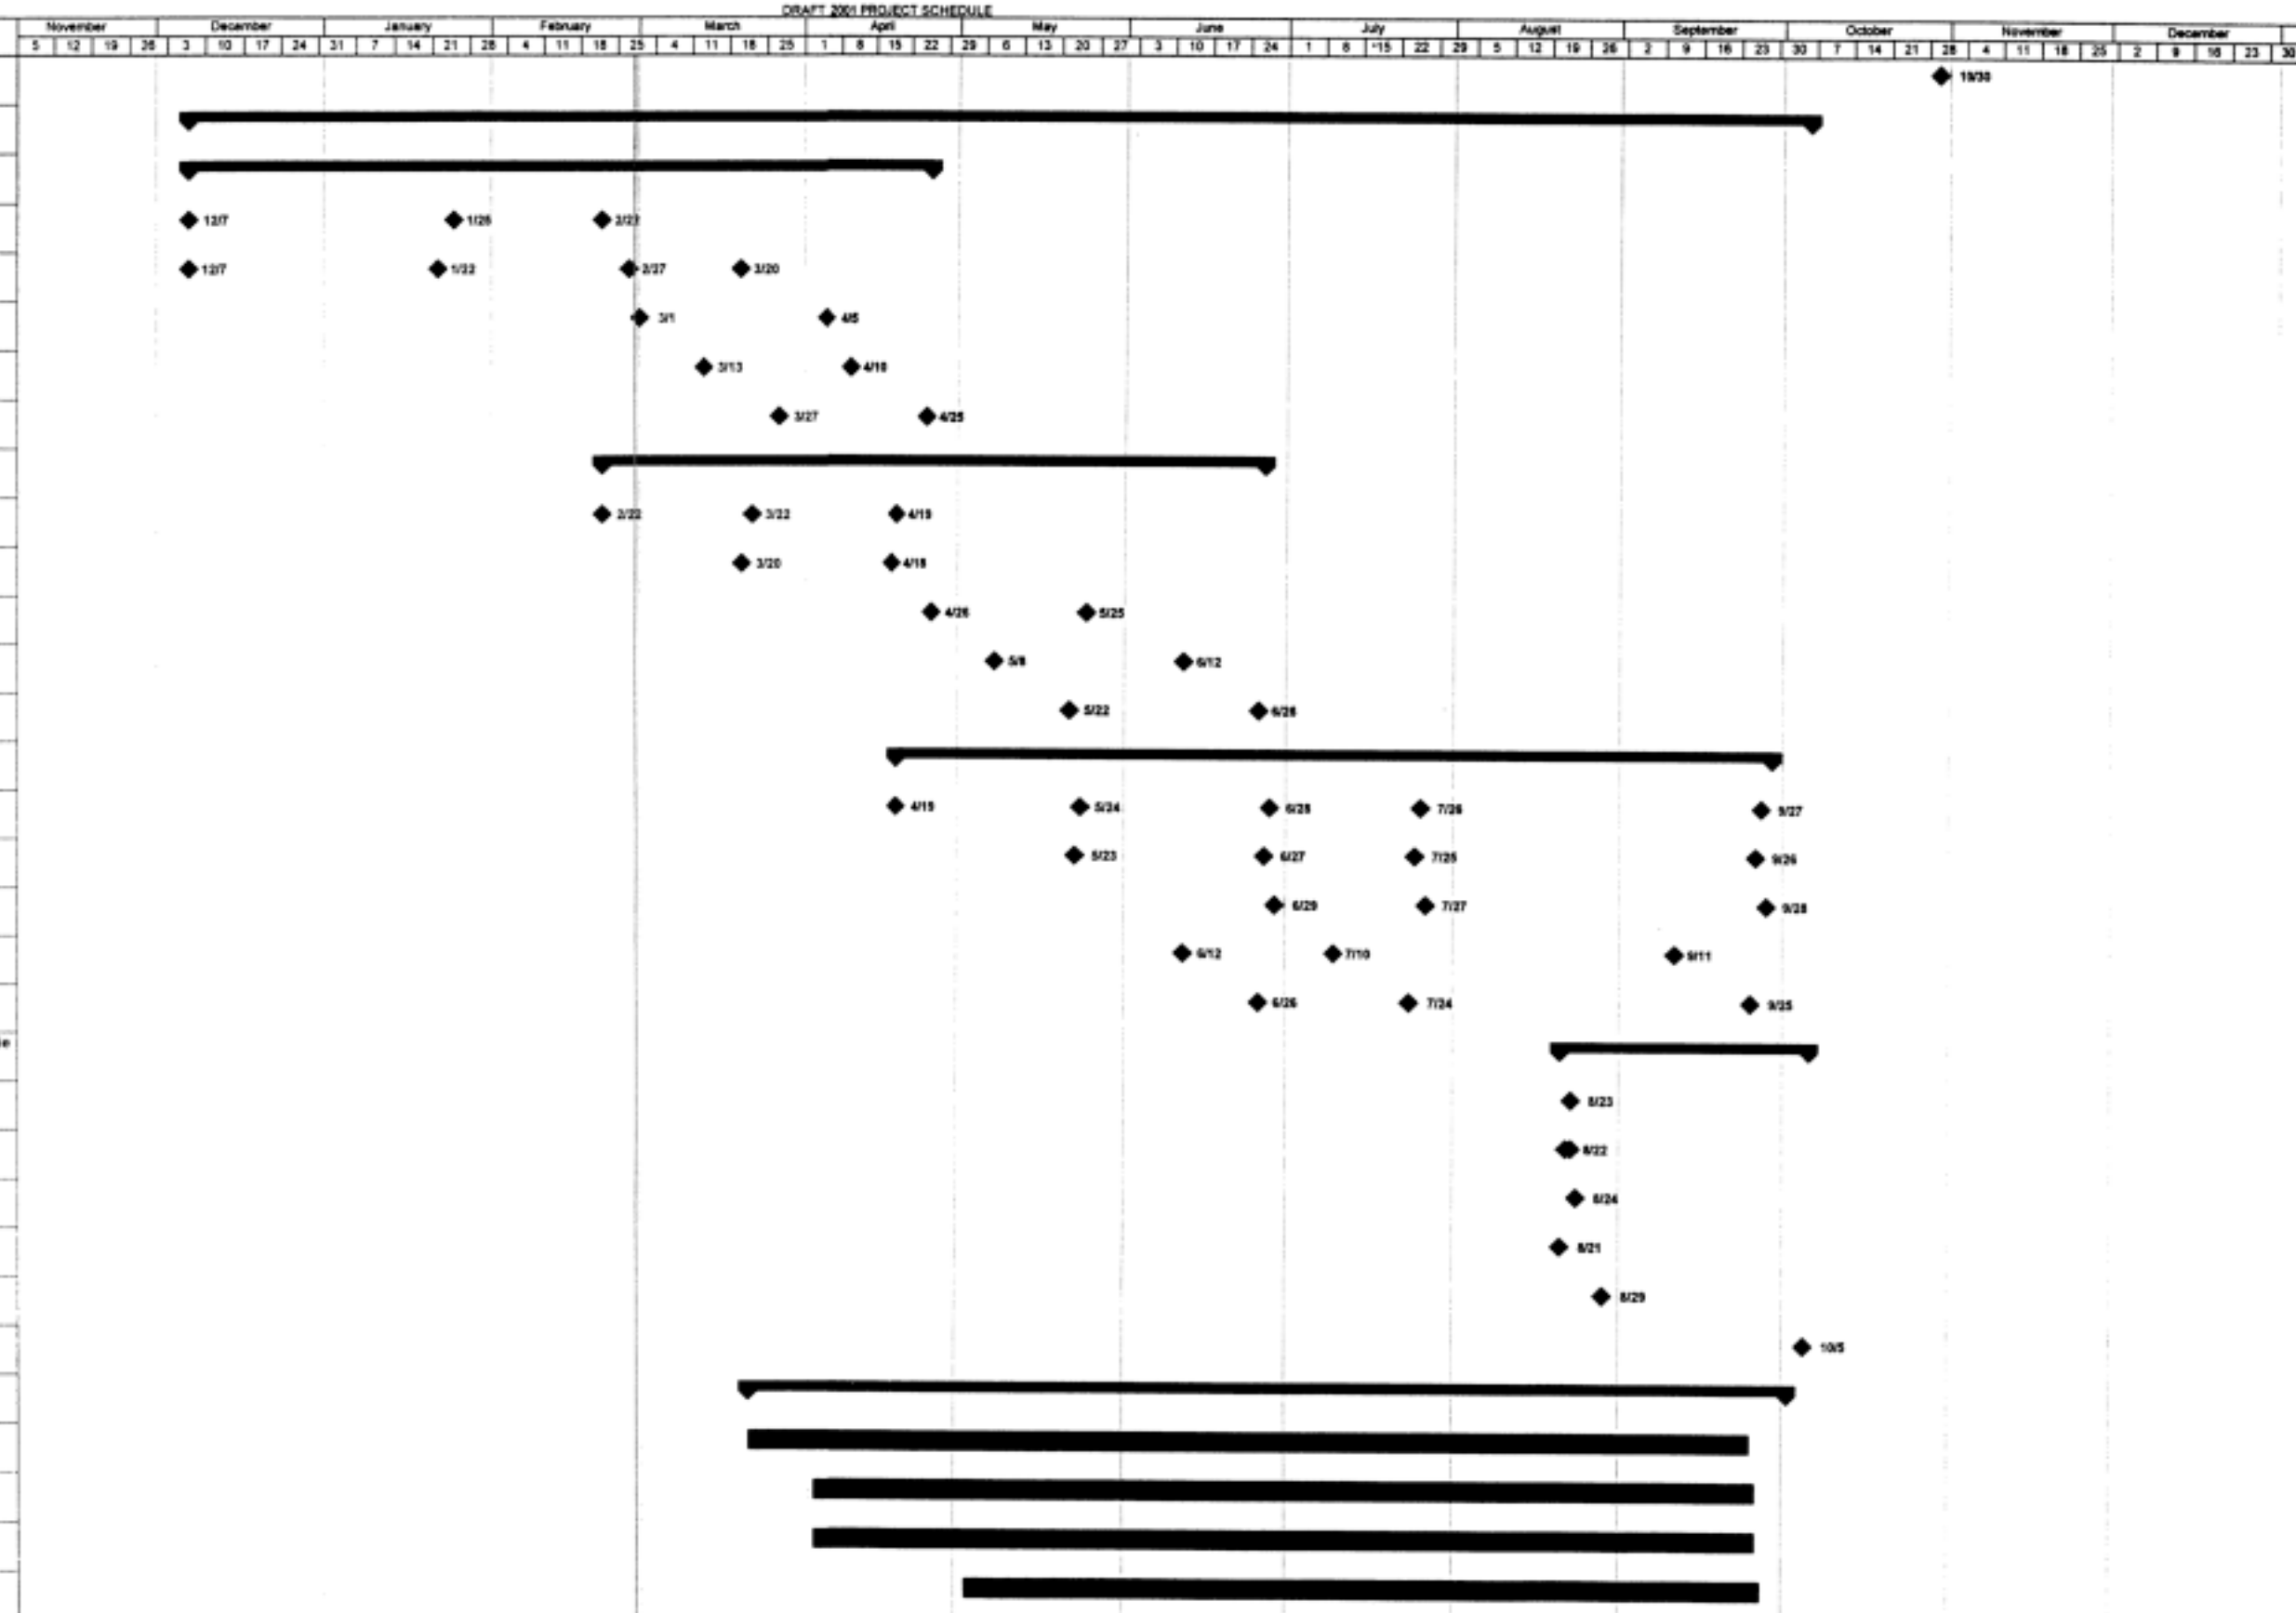

Project: OROVILLE FACILITIES REL
Date: Wed 3/28/01

Task | Task Progress | Critical Task | Critical Task Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary

OROVILLE FACILITIES RELICENSING

DRAFT 2001 PROJECT SCHEDULE

ID	Task Name
123	Land Use & Visual Resources
124	Cultural Resources
125	**Ongoing Studies**
126	**Water Quality**
127	Temperature Monitoring
128	**Aquatic Resources**
129	Hatchery Operation
130	Steelhead Snorkle Surveys and Habitat Inventory
131	Beach Seine Surveys
132	Rotary Screw Trap Sampling, Fyke Sampling, Hatchery
133	Egg Survival Studies, Spawning Aerial Surveys
134	Spawning Escapement Surveys
135	Redd De-Watering and Juvenile Stranding Surveys
136	**Operations Model Development**
137	**Interim Projects Task Force**
138	**Detailed Studies**
139	Mobilize for Detailed Field Studies
140	Initiate Field Studies Based on Study Plans

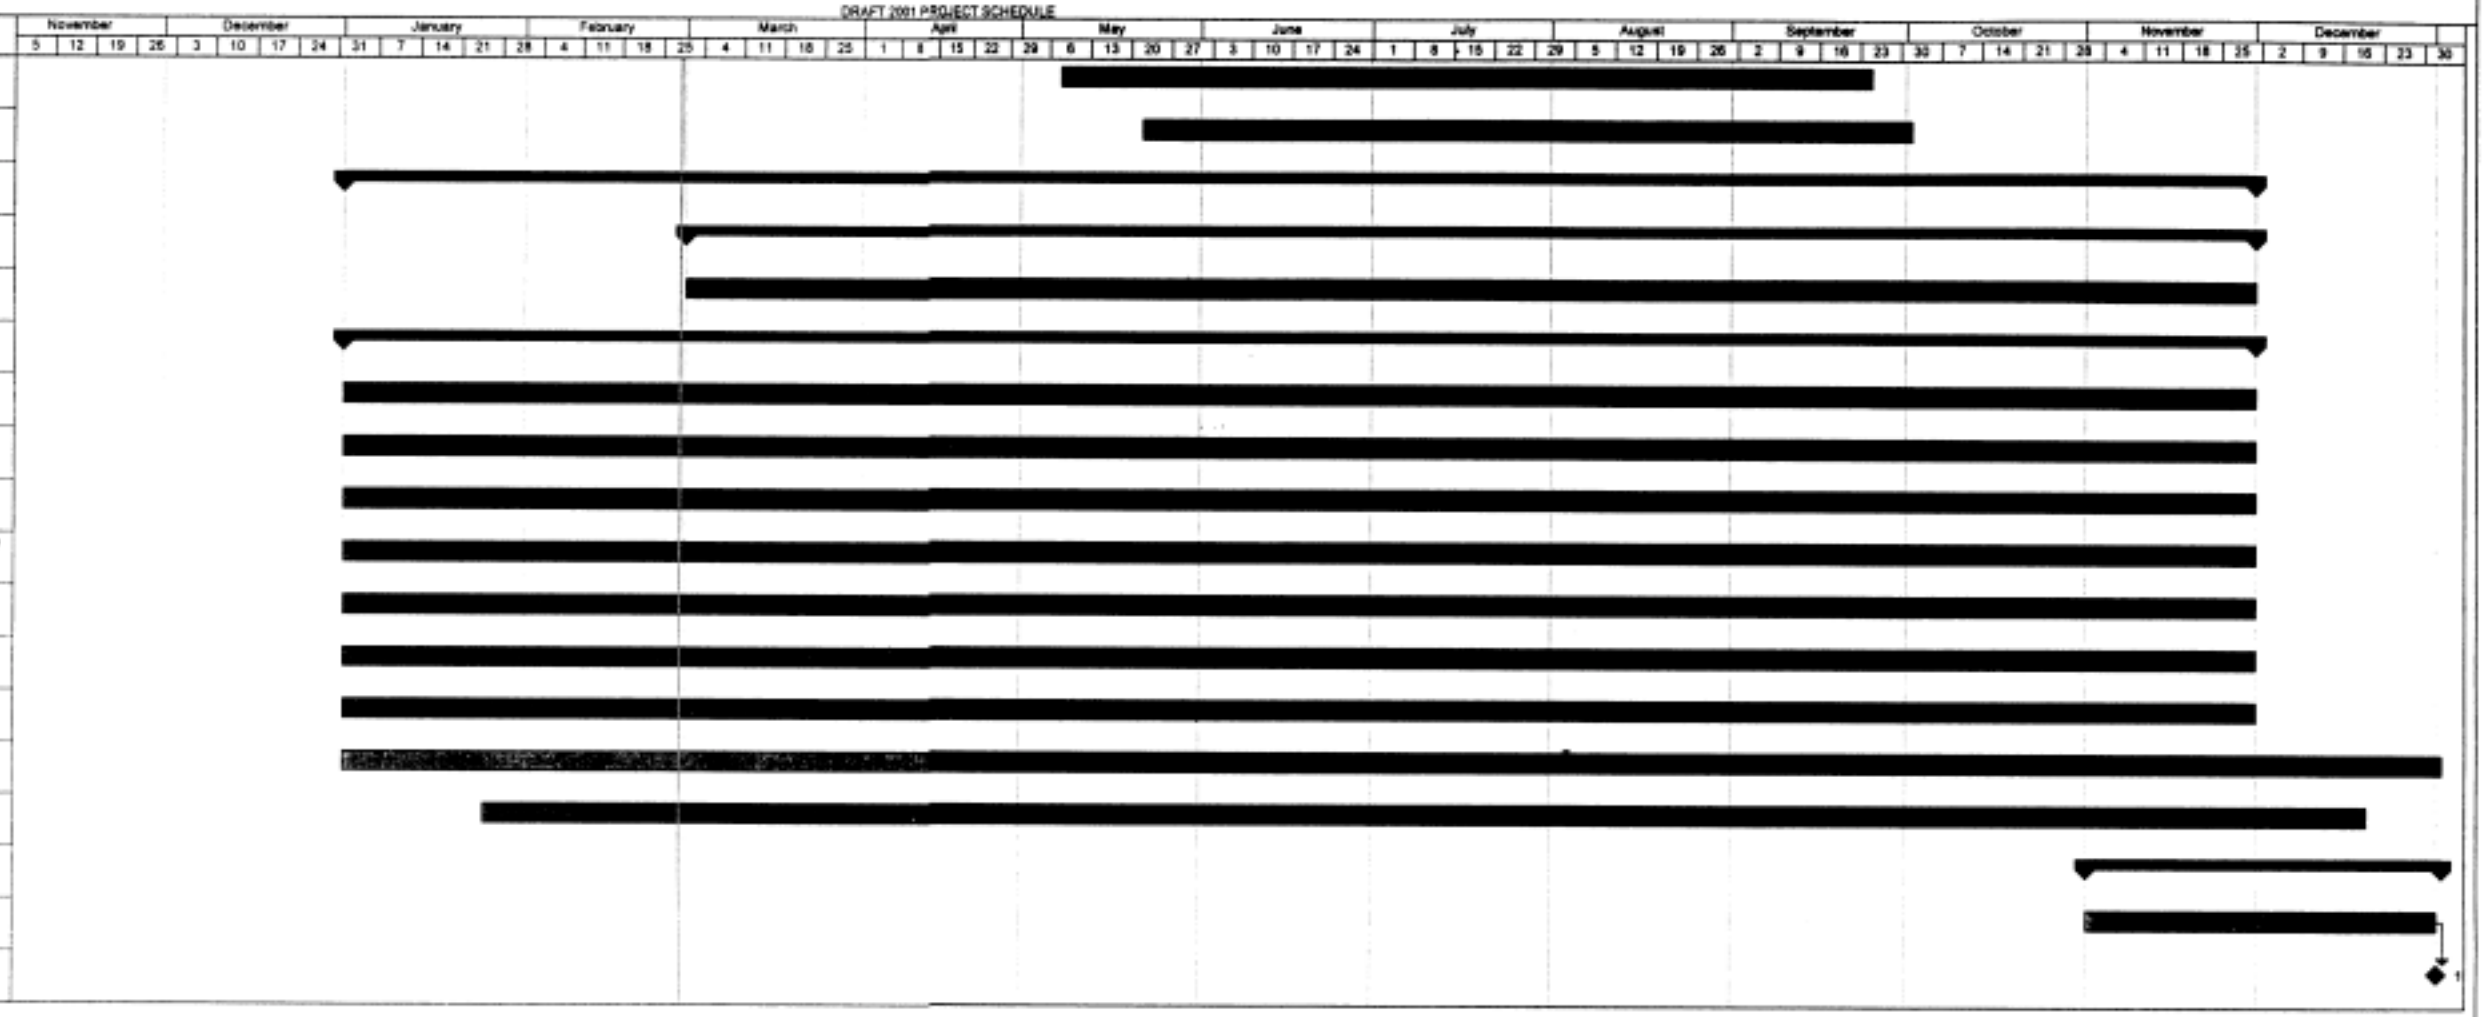

Project: OROVILLE FACILITIES REL
Date: Wed 2/28/01

Task | Task Progress | Critical Task | Critical Task Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary
